

TOWN OF PARADISE VALLEY
APPLICATION TO WORK IN THE RIGHT-OF-WAY

LOCATION OF WORK: _____

NATURE OF WORK: _____

APPLICANT: _____
(Utility Company, "A" or "K" or "L" Licensed General Contractor or Sub Contractor)

CONTACT NAME: _____ LICENSE # _____

MAILING ADDRESS: _____
(Street, City, State and Zip Code)

24 HR. PHONE: () _____ JOB FOREMAN: _____

INSURANCE COMPANY _____ Drawing # _____

DATE OF SUBMITTAL _____

NOTICE OF CONDITIONS

UNDERGROUND UTILITIES after December 31, 2005 will comply with House Bill 2256 for detectable underground location devices.

STREET CUTS require prior authorization from Richard Edwards, Engineering Department at 480-348-3528.

NOTIFY Public Works Department 24 hours in advance of START OF CONSTRUCTION 480-348-3695.

NOTIFY Public Works Department 24 hours in advance of STREET CUTS 480-348-3695.

NOTIFY Police Dept. 24 hours in advance of traffic lane closures, detours, and/or road blockages 480-948-7418.

PERMIT must be on work site during construction. Work will be stopped until Permit is present onsite.

ATTACH two sets of construction plans for review and approval. Subdivisions and water/sewer line projects require a CD of the Town-approved plans in Adobe Acrobat Reader (PDF) format.

TRENCHING, BACKFILL AND PAVEMENT REPLACEMENT shall comply with current Details and Specifications approved by the Town of Paradise Valley (per MAG specification and attached detail sheets). **NOTIFY** Public Works Department 24 hours in advance of backfilling for REQUIRED INSPECTION 480-348-3695.

TRENCH PLATTING AND BARRICADES Trench platting shall be in accordance to MAG Standard Detail 211. All barricades shall have operating lights from dusk till dawn.

LINCOLN DR and TATUM BLVD construction shall be accomplished only between the hours of 9:00 a.m. and 3:30 p.m. No barricades shall be set until 9:00 a.m. and shall be removed by 3:30 p.m. daily. The standards and specifications in Part VI of the Manual on Uniform Traffic Control Devices and the ADOT Traffic Control Manual for Highway Construction and Maintenance shall be followed.

LIABILITY INSURANCE in the amount of two million dollars, naming the Town as additional insured, is required. The original document of insurance shall be provided prior to the release of approved permit.

DUST CONTROL measures shall be enforced at all times in accordance with the Maricopa County Earth Moving Permit (projects with disturbed areas in excess of .10 acre) and attached TPV Dust Control Plan.

APPLICANT SIGNATURE _____ **Date** _____

THIS PERMIT IS ISSUED TO THE APPLICANT, SUBJECT TO THE FOLLOWING CONDITIONS:

PERFORMANCE GUARANTEE in the amount of \$500.00 (certified check or money order) is required, and has been submitted: Check No. _____. Upon completion of the project and the return of the roadway to the original condition, with adherence to MAG Specifications and all traffic control measures, **Applicant is required to call the Public Works Department at 480-348-3695 to schedule a final inspection.** Following a satisfactory inspection and approval of the project site and related work, the Performance Guarantee will be refunded in full to the Applicant.

The following daily fees shall be deducted from the Performance Guarantee, and all overages charged to the Permittee, if the Town has to provide assistance to:

- | | |
|--|----------|
| 1) Provide Traffic Control Devices (day or night) at | \$250.00 |
| 2) Provide Emergency Street Work at | \$250.00 |
| 3) Provide Any Permanent Site Restoration at | \$500.00 |
| (for work not finished by completion date) | |

All work shall be performed only by contractors holding an "A" or "K" or "L" General Contractors License.

Adequate procedures shall be followed by the Permittee for the control and safety of traffic.

If the Permittee falls behind by more than three (3) days, the Town Engineer shall be notified 480-348-3529.

TOWN COMPUTATION OF PERMIT FEES

A.C. Paving	Sq. Yd.	@ \$1.60
Concrete Sidewalk/Recreation Path	Lin. Ft.	@ \$0.50
Dust Palliative	Sq. Yd.	@ \$0.02
Concrete Valley Gutter and Apron	Lin. Ft.	@ \$0.50
Curb and Gutter	Lin. Ft.	@ \$1.00
Water Lines	Lin. Ft.	@ \$0.40
Sewer Lines	Lin. Ft.	@ \$0.40
Natural Gas Lines	Lin Ft.	@ \$1.60
Trenching	Lin. Ft.	@ \$0.20
Underground Conduit or Pipe	Lin. Ft.	@ \$0.20
Splice Pit	Each	@ \$95.00
Concrete Box Culvert (Single Barrel)	Each	@ \$142.00
Brass Cap	Each	@ \$50.00
Street Sign	Each	@ \$80.00
Traffic Control Devices (including barricades) day or night, per location	Per location	@ \$250.00
Emergency Street Work, per location	Per location	@ \$250.00
Permanent Site Restoration	Each	@ \$500.00

Ref. Article 5-5, Paradise Valley Town Code

TOWN

of

PARADISE VALLEY



Building Safety Department

6401 E Lincoln Dr
Paradise Valley, AZ 85253

(480) 348-3692
(480) 443-3236 Fax

Dust Control Plan

(for disturbed areas up to 4,356 square feet*)

Date: _____ Address: _____

Choose at least one measure per (lettered) category. (Must be done for the life of the project.)

EARTHMOVING

(It is always an option to cease operations to prevent dust.)

A) Grading / Demolition / Landscaping / Weed Control:

- Conduct watering as necessary to minimize visible emissions (increase frequency in high winds).
- Thoroughly wet the site to the depth of any cuts.

B) Trenching / Screening / Backfilling:

- Mist dust cloud resulting from trenching (increase frequency in high winds).
- Mist material after it drops from screen (increase frequency in high winds).
- Use water truck or large hose dedicated to trenching & backfilling operations.

SITE STABILIZATION/DISTURBED SURFACE AREA

A) Temporary Stabilization: (Including weekends & holidays)

- Water all areas at least twice a day until a crusted surface is formed.
- Apply chemical stabilizers.
- Additionally use wind fences / barriers / berms (not allowed as a primary measure).

When active operations will not occur for more than 15 days:

- Apply dust suppressants to all disturbed areas to maintain stabilization.
- Water all areas at least twice a day until a crusted surface is formed.
- Additionally install temporary coverings / enclosures (not allowed as a primary measure).

B) Final Stabilization: Within 8 months after active operations have ceased:

- Pave the affected area.
- Stabilize with gravel and/or recycled asphalt.
- Stabilize with vegetation.

C) Open Storage Piles:

- Apply chemical stabilizers.
- Apply water to the surface of areas of all open storage piles on a daily basis.
- Additionally install temporary coverings / enclosures (not allowed as a primary measure).

MATERIALS HANDLING/HAULING

A) Materials Handling:

- Thoroughly wet material prior to handling or loading.
- Water and/or mist material while loading to minimize visible emissions.

B) Hauling: All haul trucks must be effectively covered with a tarp or other suitable enclosure.

ROADWAYS/ACCESS POINTS

A) Unpaved haul / access roads / equipment paths: Restrict vehicle speed to 15 mph.

- Stabilize with gravel and/or recycled asphalt.
- Apply chemical dust suppressants to maintain surface stabilization.
- Water all surfaces as needed to minimize visible emissions.

B) Access Points: Vacuum or wet broom daily all dirt or mud on paved road.

- Install a stabilized construction entrance / coarse gravel pad (Required if any hauling on or off site).
- Install a wheel washer.
- Limit, restrict and/or reroute motor vehicle access.

WATER SUPPLY

A) Availability: Water storage tank Metered hydrant Hose bibb Other: _____

B) Application: By water truck(s) # _____ gal/truck _____ By hoses By sprinklers

I hereby certify that I am familiar with the operations presented above and agree to conduct all operations in compliance with the above, with Maricopa County Rule 310 and with all applicable environmental regulations.

OWNER OR AUTHORIZED AGENT SIGNATURE _____

Printed Name & Title _____

*For disturbed areas greater than 4,356 sf (1/10th of an acre) a Maricopa County Earthmoving Permit is required.

PERMIT # _____

TOWN OF PARADISE VALLEY
ENGINEERING DEPARTMENT
RIGHT-OF-WAY PERMIT
EMERGENCY DATA SHEET *

Applicant _____
(Utility Company, "A" or "K" or "L" Licensed General Contractor or Sub Contractor)

Location of Work _____

Nature of Work _____

Contact Person _____

Office No. _____ Ext. _____ Mobile _____

Pager _____ 24-Hr. No. _____

CONTRACTOR ("A" or "K" or "L" Licensed General Contractor or Sub Contractor)

Company Name _____

Contact Person _____

Office No. _____ 24-Hr. No. _____

Mobile _____ Pager _____

Alternate Contact Person _____

Mobile _____ Pager _____

TRAFFIC BARRICADE COMPANY

Company Name _____

Contact Person _____

Office No. _____ 24-Hr. No. _____

Mobile _____ Pager _____

* Provide this information with each Permit application. If unknown at time of application, fax to 480-951-3715 Attention: Richard Edwards, before start of construction.



TOWN OF
PARADISE VALLEY

6401 EAST LINCOLN DRIVE
TOWN OF PARADISE VALLEY, ARIZONA 85253-4399

PHONE: (480) 948-7411

FAX: (480) 951-3715



TDD: (480) 483-1811

OFFICE OF:

IMPORTANT NOTICE

**THE APPROVED RIGHT-OF-WAY
PERMIT MUST BE POSTED ON THE
JOB SITE DURING CONSTRUCTION.
WORK *WILL BE STOPPED* IF THE
APPROVED PERMIT IS NOT POSTED.**

A.C. PAVEMENT MATCH GRADATION & THICKNESS OF EXISTING PAVEMENT AND COURSES

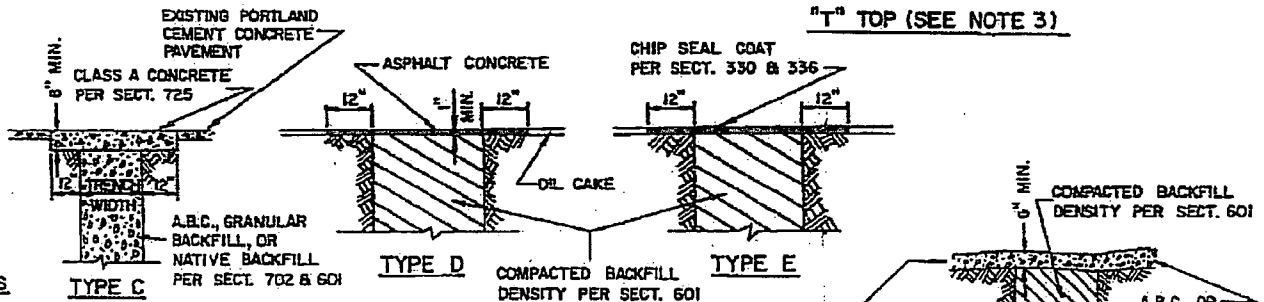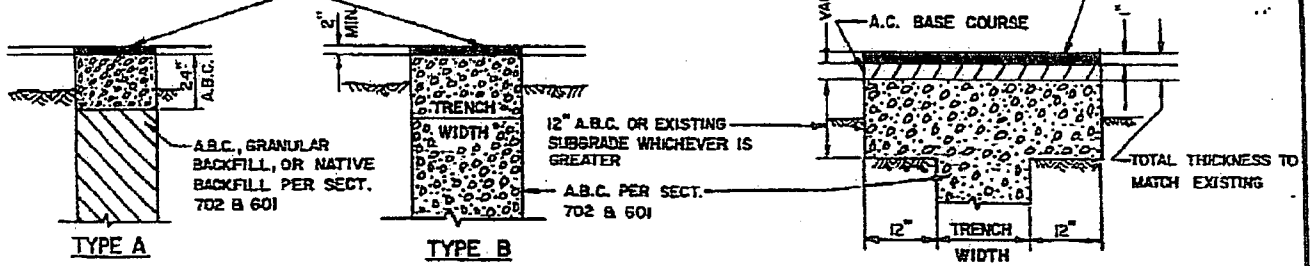


NOTES

1. BEDDING PER SECTION 601
2. ASPHALT CONCRETE SHALL BE IN ACCORDANCE WITH THE REQUIREMENTS OF SECT. 321
3. 12" LIP IS REQUIRED ON THE SIDES OF A TRENCH THAT ARE NOT PARALLEL TO THE CENTER LINE OF THE STREET.
4. TYPES D & E REQUIRE 9" OF A.B.C. AT TOP OF TRENCH WHEN THERE IS AN EXISTING BASE.

SURFACE OUTSIDE OF TRENCH LINES DAMAGED DURING CONSTRUCTION SHALL BE RESTORED TO ORIGINAL THICKNESS AND CONDITION.

DETAIL NO. 200	STANDARD DETAIL	BACKFILL, PAVEMENT & SURFACE REPLACEMENT	DETAIL NO. 200
----------------	-----------------	--	----------------

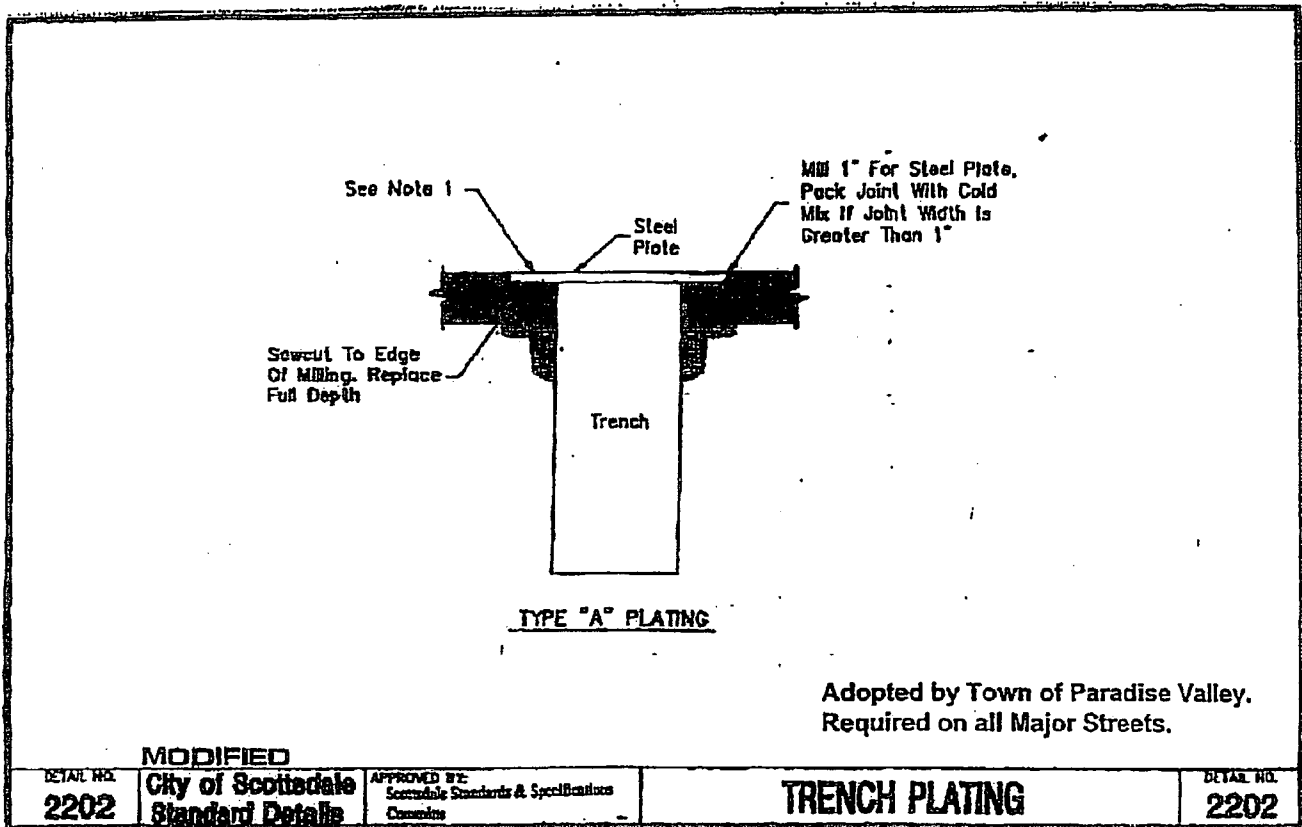

MODIFIED

DETAIL NO. 2202

City of Scottsdale
Standard Details

APPROVED BY:
Scottsdale Standards & Specifications
Committee

TRENCH PLATING

DETAIL NO. 2202
